
A MILESTONE WTITH A VIEW

PROJECT PROGRESS REFERENCE FEBRUARY 2019

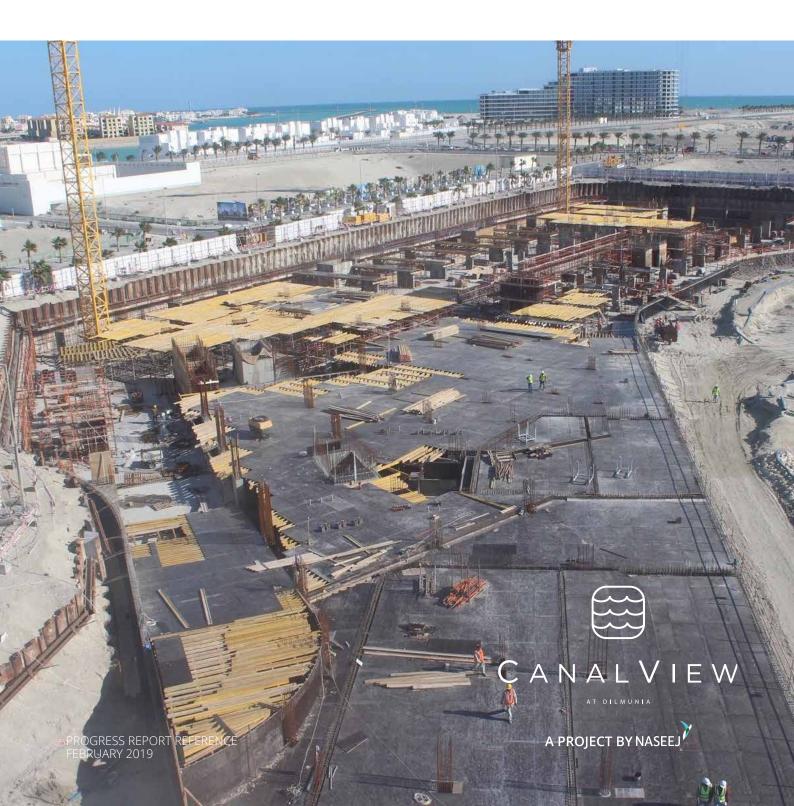

PROGRESS REPORT REFERENCE FEBRUARY 2019

WELCOME TO A NEW VIEW LIFESTYLE OF LUXURY

Investing with CanalView offers much more than the brick and mortar space that is defined by the boundary of a single apartment, it provides unlimited access to a lifestyle of luxury.

OUR PROFESSIONAL PARTNERS:



PROJECT NAME CanalView



PROJECT COMPANY

CanalView Development
Company S.P.C



DEVELOPER Naseej BSC ©



PROJECT NAME CanalView



ARCHITECT, INTERIOR & DESIGN SUPERVISION CONSULTANT

SSH Middle East



QUANTITY SURVEYOR

DG Jones



PILING CONTRACTOR

Bahrain Foundation
Construction Company W.L.L



MASTER DEVELOPER Ithmaar Development Company



PROJECT LOCATION

Dilmunia

CANALVIEW PROJECT

CanalView is a mixed use project located in Dilmunia Health Island. SSH Middle East & Kooheji Contractors were appointed as the Design and Supervision Consultant and Main Contractor respectively.


The piling works were completed by Bahrain Foundation Construction Company under the supervision of SSH. After the appointment of Main Contractor in May 2018, around 35,000 m² of excavated fill was removed and 300 linear meters of retention sheet piling installed to enable basement construction to commence.





PROGRESS REPORT REFERENCE FEBRUARY 2019

SUMMARY OF CANALVIEW'S CONSTRUCTION PROGRESS

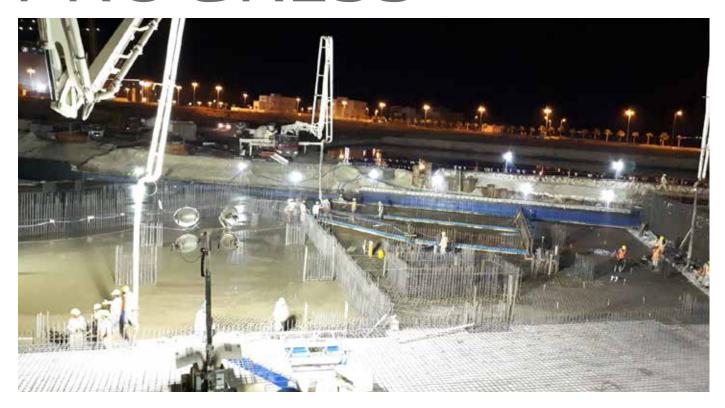

Progress as per plan Progress actual at site

9.7%

The project is progressing in a good pace to meet the target milestones.

- Percentage progress as per plan: 9.70%
- Percentage progress actual at site: 9.70%

SUMMARY OF CONSTRUCTION WORKS ON SITE

1

Work completed and in progress at site till 15th January 2019

- Concreting of piles complete
- Concreting of pile caps complete
- Concreting of raft slab foundation complete
- Concreting of basement carpark columns in progress (60% complete)
- Shuttering works for basement carpark roof slab in progress

2

Activities expected to complete by end of March 2019

- Concreting of basement carpark roof slab
- Concreting of upper retail columns

3

Master Developer updates:

- Main canal ground preparation works complete and canal basin works due to commence.
- · Other developments in Dilmunia island

1

WORK COMPLETED AND IN PROGRESS AT SITE TILL 15TH JANUARY 2019

Concreting of piles complete





Concreting of pile caps complete





Concreting of raft slab foundation complete





Concreting of basement carpark columns in progress (60% complete)







Shuttering works for basement carpark roof slab in progress







2 WORK EXPECTED TO BE COMPLETED BY END OF MARCH 2019

Concreting of basement carpark roof slab



Concreting of upper retail columns



MASTER DEVELOPER UPDATES



Ithmaar Development Company (IDC), the Development Manager for Dilmunia at Bahrain announced the award of the early works package for the Dilmunia Grand Canal & Marina. The Grand Canal will cut through the entire stretch of Dilmunia in a semi-circular route, making it Bahrain's largest man-made water body and providing breathtaking vistas to surrounding developments within Dilmunia, and one of Bahrain's longest continuous promenades to residents and visitors of the island.



Preparation of the main canal



PROGRESS REPORT REFERENCE FEBRUARY 2019

Canal Bed Soil Improvement in Process





Other projects progress in Dilmunia island







Dilmunia mall progress











STAY CONNECTED WITH CANALVIEW







www.canalview.bh







This report has been published by:
Naseej BSC (c)
Bahrain Financial Harbour
Contact: +973 16 557999
www.naseej.bh
